



LBCC Bond Program Master Schedule

Status as of July 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q

Long Beach Community College Bond Program Schedule - July 1, 2019

Liberal Arts Campus

Building J - Auditorium

Design Building J	176	01-Oct-15 A	24-Mar-16 A
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A
DSA Building J	398	03-Sep-16 A	06-Oct-17 A
Bid / Award Building J	89	07-Oct-17 A	04-Jan-18 A
Construction Building J (Spring 2018 - Fall 2019)	670	16-Jan-18 A	16-Nov-19
FF&E / Move Management from Building J from Public Theater & Building FF	276	18-Sep-19	19-Jun-20
Expected Substantial Completion Building J	0		16-Nov-19
Ready to Hold Classes Building J (Fall 2020)	0		19-Jun-20

Lew Davis Sidewalk Replacement Project

Bid / Award Lew Davis Sidewalk Replacement	89	11-Apr-19 A	08-Jul-19
NTP Lew Davis Sidewalk Replacement	0	09-Jul-19	
Construction Lew Davis Sidewalk Replacement	40	09-Jul-19	17-Aug-19
Expected Substantial Completion	0		17-Aug-19

Kinesiology Labs & Aquatics Center

Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A
Design Kinesiology Labs & Aquatic Center	615	01-Jun-17 A	06-Feb-19 A
DSA Kinesiology Labs & Aquatic Center	195	29-Jan-19 A	11-Aug-19
Bid / Award Kinesiology Labs & Aquatic Center	106	12-Aug-19	25-Nov-19
NTP Kinesiology Labs & Aquatic Center	0	05-Dec-19	
Phase 2 Softball Complex	360	05-Dec-19	28-Nov-20
Phase 1 Aquatic Complex & North Fields	530	05-Dec-19	17-May-21
Phase 3 Parking Lot etc.	45	29-Nov-20	12-Jan-21
FF&E / Move Management Kinesiology Labs & Aquatic Center	194	17-Feb-21	29-Aug-21
Final Completion Kinesiology Labs & Aquatic Center	0		16-Jun-21
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)	0		29-Aug-21

Building X - Central Plant Expansion


Design	413	23-Jan-18 A	12-Mar-19 A
DSA LAC Central Plant	111	13-Apr-19 A	01-Aug-19
Bid / Award	95	02-Aug-19	04-Nov-19
Construction LAC Central Plant	130	12-Nov-19	20-Mar-20
Expected Substantial Completion	0		20-Mar-20

LAC Site Barrier Removal

Design Campus Improvements	838	12-Sep-17 A	28-Dec-19
DSA Review LAC Site Barrier Removal	183	29-Dec-19	28-Jun-20
Bid / Award LAC Site Barrier Removal	92	29-Jun-20	28-Sep-20
Construction LAC Site Barrier Removal	518	06-Oct-20	07-Mar-22
Expected Substantial Completion	0		07-Mar-22

LAC Building Barrier Removal

Design Campus Improvements	866	12-Sep-17 A	25-Jan-20
DSA Review LAC Building Barrier Removal	182	26-Jan-20	25-Jul-20
Bid / Award LAC Building Barrier Removal	90	26-Jul-20	23-Oct-20
Construction LAC Building Barrier Removal	518	12-Nov-20	13-Apr-22
Expected Substantial Completion	0		13-Apr-22

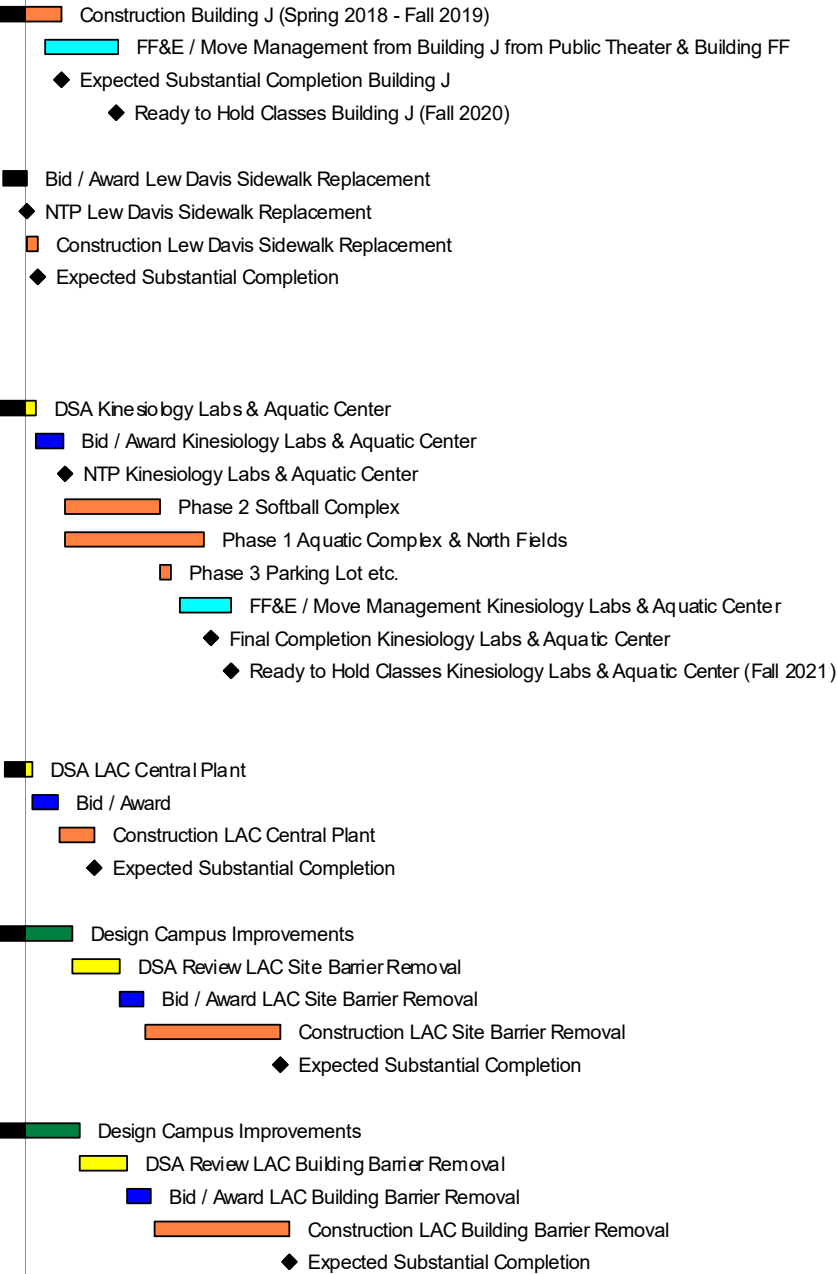

PRE Bid / Award CONST Actual
DESIGN DSA FF&E Milestone Milestone



LBCC Bond Program Master Schedule

Status as of July 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Building B Tenant Improvement (Building M Swing Space)																					
Bid / Award Building B Swing Space for Building M	86	13-Apr-19 A	07-Jul-19	■ Bid / Award Building B Swing Space for Building M																	
NTP Construction	0	10-Jul-19		◆ NTP Construction																	
Construction Swing Space Building B Renovation 2nd Floor & 3rd Floor	30	10-Jul-19*	08-Aug-19	■ Construction Swing Space Building B Renovation 2nd Floor & 3rd Floor																	
Construction Swing Space Building B Renovation 1st Floor & Non-Occupied Rooms	85	10-Jul-19	02-Oct-19	■ Construction Swing Space Building B Renovation 1st Floor & Non-Occupied Rooms																	
Expected Substantial Completion Swing Space Building B Renovation	0		02-Oct-19	◆ Expected Substantial Completion Swing Space Building B Renovation																	
Lot A Portable Buildings (Building M Swing Space)																					
Bid / Award Portable Building Lot A (Board Award July 24, 2019)	110	15-Apr-19 A	02-Aug-19	■ Bid / Award Portable Building Lot A (Board Award July 24, 2019)																	
Construction Swing Space Portable Building Lot A	90	05-Aug-19	02-Nov-19	■ Construction Swing Space Portable Building Lot A																	
NTP Construction	0	05-Aug-19		◆ NTP Construction																	
Expected Substantial Completion Swing Space Portable Building Lot A	0		02-Nov-19	◆ Expected Substantial Completion Swing Space Portable Building Lot A																	
Building M - Liberal Arts																					
Pre-Design Building M	329	01-Aug-17 A	26-Jun-18 A																		
Award DBE Building M	120	27-Jun-18 A	25-Oct-18 A																		
Design and DSA Review Building M	495	05-Nov-18 A	13-Mar-20	■ Design and DSA Review Building M																	
FF&E / Move Management Swing Spaces Building B for Building M	212	06-Jun-19 A	03-Jan-20	■ FF&E / Move Management Swing Spaces Building B for Building M																	
Move Into Swing Spaces for Building M (Dec 2019 / Jan 2020)	20	15-Dec-19*	03-Jan-20	■ Move Into Swing Spaces for Building M (Dec 2019 / Jan 2020)																	
NTP Construction Building M	0	14-Mar-20		◆ NTP Construction Building M																	
Construction Substantial Completion Building M	596	14-Mar-20	30-Oct-21	■ Construction Substantial Completion Building M																	
FF&E / Move Management Building M	273	01-Oct-21	01-Jul-22	■ FF&E / Move Management Building M																	
Expected Substantial Completion Building M	0		30-Oct-21	◆ Expected Substantial Completion Building M																	
Ready to Hold Classes Building M (Fall 2022)	0		01-Jul-22	◆ Ready to Hold Classes Building M (Fall 2022)																	
EEM-2A - Energy and Portable Water Reductions - LAC (TBD)																					
Design EEM-2A	180	01-Apr-20*	27-Sep-20	■ Design EEM-2A																	
DSA EEM-2A	260	28-Sep-20	14-Jun-21	■ DSA EEM-2A																	
Bid / Award EEM-2A	90	15-Jun-21	12-Sep-21	■ Bid / Award EEM-2A																	
Construction EEM-2A	365	13-Sep-21	12-Sep-22	■ Construction EEM-2A																	
EEM-2C - Thermal Storage Strategy - Bldg P Attic (TBD)																					
Design EEM-2C	180	01-Apr-20*	27-Sep-20	■ Design EEM-2C																	
DSA EEM-2C	160	28-Sep-20	06-Mar-21	■ DSA EEM-2C																	
Bid / Award EEM-2C	90	07-Mar-21	04-Jun-21	■ Bid / Award EEM-2C																	
Construction EEM-2C	160	05-Jun-21	11-Nov-21	■ Construction EEM-2C																	
Building E - College Center																					
Design Building E	432	03-Aug-20	08-Oct-21	■ Design Building E																	
DSA Review Swing Space for Building E	280	17-Jul-21	22-Apr-22	■ DSA Review Swing Space for Building E																	
DSA Review Building E	280	09-Oct-21	15-Jul-22	■ DSA Review Building E																	
Bid / Award Swing Space for Building E	93	23-Apr-22	24-Jul-22	■ Bid / Award Swing Space for Building E																	
Bid / Award Building E	91	16-Jul-22	14-Oct-22	■ Bid / Award Building E																	
Construction Swing Space for Building E	75	25-Jul-22	07-Oct-22	■ Construction Swing Space for Building E																	
FF&E / Move Management Building B Swing Space for Building E	180	09-Aug-22	04-Feb-23	■ FF&E / Move Management Building B Swing Space for Building E																	
Expected Substantial Completion Swing Space for Building E	0		07-Oct-22	◆ Expected Substantial Completion Swing Space for Building E																	
Punchlist Swing Space for Building E	30	08-Oct-22	06-Nov-22	■ Punchlist Swing Space for Building E																	
Move Into Swing Space Building B for Building E (Dec 2022 / Jan 2023)	30	16-Dec-22	14-Jan-23	■ Move Into Swing Space Building B for Building E (Dec 2022 / Jan 2023)																	
NTP	0	20-Jan-23		◆ NTP																	
Construction Building E	610	20-Jan-23	20-Sep-24	■ Construction Building E																	
FF&E / Move Management Building E	200	23-Jun-24	08-Jan-25	■ FF&E / Move Management Building E																	
Expected Substantial Completion	0		20-Sep-24	◆ Expected Substantial Completion																	

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone



LBCC Bond Program Master Schedule

Status as of July 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Ready to Hold Classes Building E (Spring 2025)	0		08-Jan-25																		
Building O2 - Economic & Workforce Development/Foundation				◆ Ready to Hold Classes Building E (Spring 2025)																	
Pre-Design Building O2	180	14-Apr-23*	10-Oct-23																		
Design Building O2	280	11-Oct-23	16-Jul-24																		
DSA Review Building O2	280	17-Jul-24	22-Apr-25																		
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25																		
Bid / Award Building O2	90	23-Apr-25	21-Jul-25																		
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25																		
Move Into Swing Space Building B for Building O2	20	22-Jun-25	11-Jul-25																		
NTP Construction Building O2	0	27-Jul-25																			
Construction Building O2	520	27-Jul-25	28-Dec-26																		
FF&E / Move Management from Building B to Building O2	209	09-Dec-26	05-Jul-27																		
Expected Substantial Completion Building O2	0		28-Dec-26																		
Building G - Music																					
Pre-Design Building G	216	04-Aug-25*	07-Mar-26																		
Design Building G	273	08-Mar-26	05-Dec-26																		
DSA Review Building G	280	06-Dec-26	11-Sep-27																		
Design Swing Space for Building G	67	01-Jun-27	06-Aug-27																		
Bid / Award Swing Space for Building G	89	07-Aug-27	03-Nov-27																		
Bid / Award Building G	90	12-Sep-27	10-Dec-27																		
Construction Swing Space Building for G	40	04-Nov-27	13-Dec-27																		
Expected Substantial Completion Swing Space Building for G	0		13-Dec-27																		
Move Into Swing Space Building B for Building G	15	14-Dec-27	28-Dec-27																		
Construction Building G	750	29-Dec-27	16-Jan-30																		
Expected Substantial Completion Building G	0		16-Jan-30																		
FF&E / Move Management Building G from Building B	162	17-Jan-30	27-Jun-30																		
Ready to Hold Classes Building G	0		27-Jun-30																		
Building H - Theater Arts																					
Pre-Design Building H	217	04-Aug-25*	08-Mar-26																		
Design Building H	273	09-Mar-26	06-Dec-26																		
DSA Review Building H	280	07-Dec-26	12-Sep-27																		
Bid / Award Building H	92	13-Sep-27	13-Dec-27																		
Move Into Public Theater from Building H	20	14-Dec-27	02-Jan-28																		
Construction Building H	750	29-Dec-27	16-Jan-30																		
Expected Substantial Completion	0		16-Jan-30																		
FF&E / Move Management Building H from Building Public Theater	146	17-Jan-30	11-Jun-30																		
Ready to Hold Classes Building H	0		11-Jun-30																		
Building K - Art																					
Pre-Design Building K	210	06-Aug-28*	03-Mar-29																		
Design Building K	224	04-Mar-29	13-Oct-29																		
DSA Review Building K	280	14-Oct-29	20-Jul-30																		
Bid / Award Building K	90	21-Jul-30	18-Oct-30																		
Move Into Swing Space Building B for Building K	10	19-Dec-30	28-Dec-30																		
NTP Construction Building K	0	29-Dec-30																			
Construction Building K	390	29-Dec-30	22-Jan-32																		
FF&E / Move Management Building K from Building B	251	25-Oct-31	01-Jul-32																		
Expected Substantial Completion Building K	0		22-Jan-32																		

- PRE
- Bid /Award
- CONST
- Actual
- DESIGN
- DSA
- FF&E
- ◆

 Milestone
- ◆

 Milestone




LBCC Bond Program Master Schedule

Status as of July 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Ready to Hold Classes Building K	0		01-Jul-32																		
Building R - Primary Gymnasium																					
Pre-Design Building R	145	08-Jul-29*	29-Nov-29																		
Design Building R	363	30-Nov-29	27-Nov-30																		
DSA Review Building R	280	28-Nov-30	03-Sep-31																		
Bid / Award Building R	90	04-Sep-31	02-Dec-31																		
NTP Construction Building R	0	08-Dec-31																			
Construction Building R	730	08-Dec-31	06-Dec-33																		
FF&E / Move Management Building R	180	10-Jul-33	05-Jan-34																		
Expected Substantial Completion Building R	0		06-Dec-33																		
Ready to Hold Classes Building R	0		05-Jan-34																		
Building Q - Secondary Gymnasium																					
Pre-Design Building	320	16-Jun-31*	30-Apr-32																		
Design Building	246	01-May-32	01-Jan-33																		
DSA Review Building	280	02-Jan-33	08-Oct-33																		
Bid / Award Building	90	09-Oct-33	06-Jan-34																		
NTP Construction Building	0	12-Jan-34																			
Construction Building	640	12-Jan-34	13-Oct-35																		
FF&E / Move Management Building Q	195	16-Jun-35	27-Dec-35																		
Expected Substantial Completion Building	0		13-Oct-35																		
Ready to Hold Classes Building	0		27-Dec-35																		
Building B - Tech Studies																					
Pre-Design Building	200	18-Aug-32*	05-Mar-33																		
Design Building	276	06-Mar-33	06-Dec-33																		
DSA Review Building	280	07-Dec-33	12-Sep-34																		
Bid / Award Building	90	13-Sep-34	11-Dec-34																		
NTP Construction Building	0	12-Dec-34																			
Construction Building	730	28-Dec-34	26-Dec-36																		
Expected Substantial Completion Building	0		26-Dec-36																		
Building F - Demo Family/Consumer Education/New Courtyard																					
Design Building F	245	03-Mar-35*	02-Nov-35																		
DSA Review Building F	160	03-Nov-35	10-Apr-36																		
Bid / Award Building F	55	11-Apr-36	04-Jun-36																		
Move Into Building B from Building F	180	27-Dec-36	24-Jun-37																		
Demo & Courtyard Building F	365	25-Jun-37	24-Jun-38																		
Building O1 - IITS/ Warehouse																					
Pre-Design Building	183	02-May-35*	31-Oct-35																		
Design Building	244	01-Nov-35	01-Jul-36																		
DSA Review Building	280	02-Jul-36	07-Apr-37																		
Bid / Award Building	90	08-Apr-37	06-Jul-37																		
NTP Construction Building	0	12-Jul-37																			
Construction Building O1	420	12-Jul-37	04-Sep-38																		
FF&E / Move Management Building O1 from Building O2	213	08-May-38	06-Dec-38																		
Expected Substantial Completion Building O1	0		04-Sep-38																		
Building S - Stadium																					
Pre-Design Building	200	01-May-35*	16-Nov-35																		
Design Building	365	22-Nov-35	20-Nov-36																		

- PRE
- DESIGN
- Bid /Award
- DSA
- CONST
- FF&E
- Actual
- Milestone

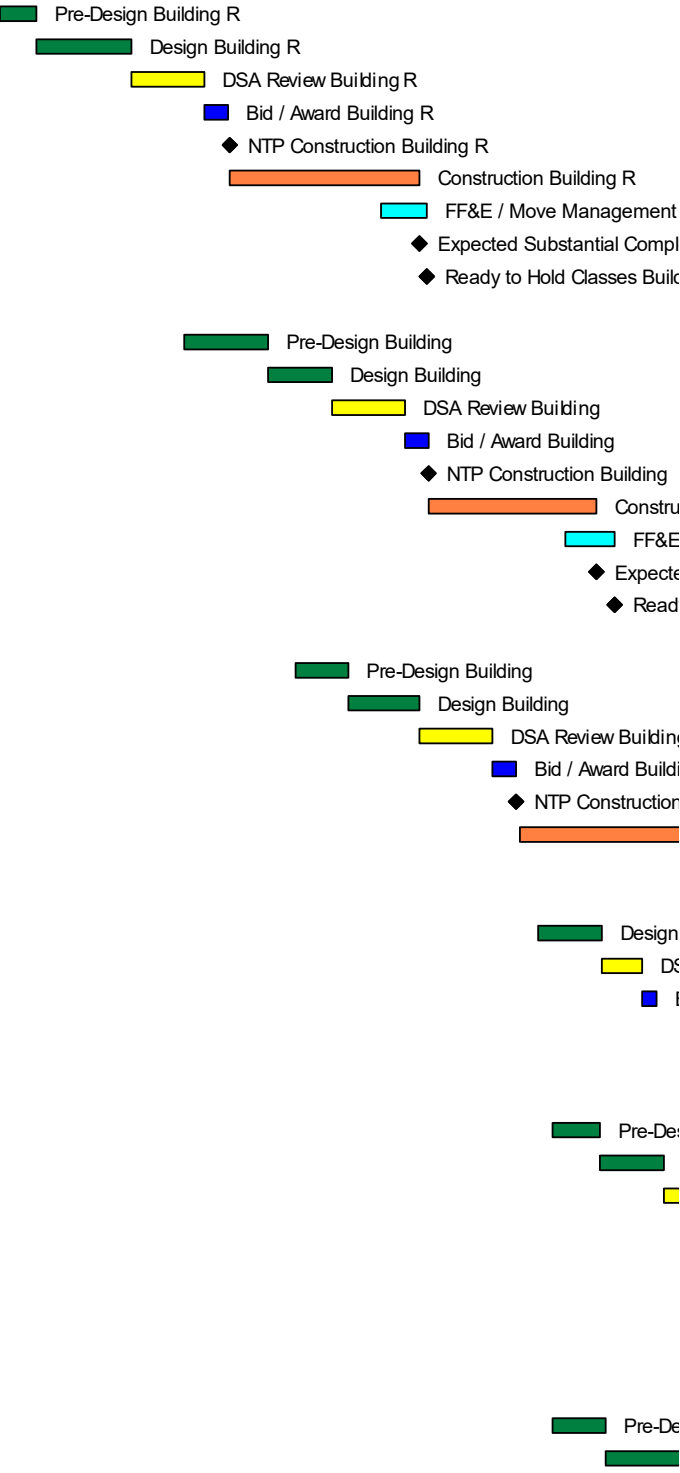



LBCC Bond Program Master Schedule

Status as of July 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
DSA Review Building S	280	21-Nov-36	27-Aug-37																		
Bid / Award Building S	90	28-Aug-37	25-Nov-37																		
Construction Swing Space Building for S	90	28-Aug-37	25-Nov-37																		
Expected Substantial Completion Swing Space Building for S	0		25-Nov-37																		
Move Into Swing Space Building TBD from Building S	15	06-Dec-37	20-Dec-37																		
NTP Construction Building S	0	21-Dec-37																			
Construction Building S	700	21-Dec-37	20-Nov-39																		
FF&E / Move Management Building from Building TBD to Building S	250	24-Jul-39	29-Mar-40																		
Expected Substantial Completion Building S	0		20-Nov-39																		
Punchlist Building S	30	21-Nov-39	20-Dec-39																		
Ready to Hold Classes Building S	0		29-Mar-40																		
Building CDC - Child Development Center																					
Pre-Design Building	49	01-Jun-37*	19-Jul-37																		
Design Building	154	20-Jul-37	20-Dec-37																		
DSA Review Building	280	21-Dec-37	26-Sep-38																		
Bid / Award Building	90	27-Sep-38	25-Dec-38																		
NTP Construction Building	0	26-Dec-38																			
Construction Building	290	26-Dec-38	11-Oct-39																		
FF&E / Move Management	201	13-Jun-39	30-Dec-39																		
Expected Substantial Completion Building	0		11-Sep-39																		
Pacific Coast Campus																					
PCC Building Barrier Removal																					
Bid / Award Building Barrier Removal	117	20-Feb-18 A	17-Jun-18 A																		
Construction - Phase 0	69	24-Jul-18 A	01-Oct-18 A																		
Construction - Phase 1-A	143	10-Sep-18 A	31-Jan-19 A																		
Construction - Phase 1-B	227	10-Sep-18 A	25-Apr-19 A																		
Construction - Phase 2	126	18-Jan-19 A	24-May-19 A																		
Construction - Phase 3	60	06-Jun-19 A	04-Aug-19																		
Construction - Phase 4	35	05-Aug-19	08-Sep-19																		
Expected Substantial Completion AI Phases	0		08-Sep-19																		
Building P2 - PCC Parking Structure																					
Design Parking Structure	224	16-Jul-18 A	25-Feb-19 A																		
DSA Review Parking Structure	217	16-Jan-19 A	20-Aug-19																		
NTP Construction Parking Structure	0	21-Aug-19																			
Construction Parking Structure	400	21-Aug-19	23-Sep-20																		
Expected Substantial Completion Parking Structure	0		23-Sep-20																		
Closeout Parking Structure	30	24-Sep-20	23-Oct-20																		
Building MM - Construction Trades Ph 1																					
DSA Review Building MM Ph 1	254	10-Jan-19 A	20-Sep-19																		
Approve Working Documents and Proceed to Bid Ph 1	52	31-Aug-19	21-Oct-19																		
Approval to Award Construction Contract	170	22-Oct-19	08-Apr-20																		
Construction Building MM Ph 1	420	09-Apr-20	02-Jun-21																		
FF&E / Move Management Building MM for Building MM Ph 1	192	03-Feb-21	14-Aug-21																		
Expected Substantial Completion Building MM Ph 1	0		02-Jun-21																		
Ready to Hold Classes Building MM Ph 1 (Fall 2021)	0		14-Aug-21																		
EEM-2A - Energy and Portable Water Reductions - PCC (TBD)																					

- PRE
- Bid /Award
- CONST
- Actual
- DESIGN
- DSA
- FF&E
- Milestone
- Milestone

- Construction - Phase 3
- Construction - Phase 4
- Expected Substantial Completion AI Phases
- DSA Review Parking Structure
- NTP Construction Parking Structure
- Construction Parking Structure
- Expected Substantial Completion Parking Structure
- Closeout Parking Structure
- DSA Review Building MM Ph 1
- Approve Working Documents and Proceed to Bid Ph 1
- Approval to Award Construction Contract
- Construction Building MM Ph 1
- FF&E / Move Management Building MM for Building MM Ph 1
- Expected Substantial Completion Building MM Ph 1
- Ready to Hold Classes Building MM Ph 1 (Fall 2021)



LBCC Bond Program Master Schedule

Status as of July 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Design EEM-2A	180	01-Apr-20*	27-Sep-20																		
DSA EEM-2A	260	28-Sep-20	14-Jun-21																		
Bid / Award EEM-2A	90	15-Jun-21	12-Sep-21																		
Construction EEM-2A	365	13-Sep-21	12-Sep-22																		
Building MM - Construction Trades Ph 2																					
Design Building MM Ph 2	454	01-Oct-20	28-Dec-21																		
DSA Review Building MM Ph 2	280	29-Dec-21	04-Oct-22																		
Bid / Award Building Building MM Ph 2	90	05-Oct-22	02-Jan-23																		
Construction Building MM Ph 2	390	03-Jan-23	27-Jan-24																		
FF&E / Move Management Building MM from Building MM Ph 2	238	29-Nov-23	23-Jul-24																		
Expected Substantial Completion Building MM Ph 2	0		27-Jan-24																		
Ready to Hold Classes Building MM Ph 2 (Fall 2024)	0		23-Jul-24																		
Building OO - Humanities																					
Design Building Humanities	608	01-Oct-20*	31-May-22																		
DSA Review Building Humanities	280	01-Jun-22	07-Mar-23																		
Bid / Award Building Humanities	90	08-Mar-23	05-Jun-23																		
NTP Construction Building Humanities	0		10-Jun-23																		
Construction Building Humanities	770	11-Jun-23	19-Jul-25																		
FF&E / Move Management Building Humanities from Building Humanities	270	11-Apr-25	05-Jan-26																		
Expected Substantial Completion Building Humanities	0		19-Jul-25																		
Ready to Hold Classes Building Humanities (Spring 2026)	0		05-Jan-26																		
Building FF - Demo Fine Arts & Senior Center/Turnabout																					
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23																		
DSA Review Building FF	280	09-Mar-23	13-Dec-23																		
Bid / Award Building FF Demo & Turnabout	86	14-Dec-23	08-Mar-24																		
Construction Building FF Demo	155	09-Mar-24	10-Aug-24																		
PCC Walkways & Wayfinding																					
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41																		
District Wide																					
Joint Use Facility w/ LBUSD & CSULB #12																					
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21																		
Energy/Water Conservation Projects																					
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41																		
Districtwide Solar Projects																					
Pre-Design, Criteria Documents, RFP	360	21-Mar-19 A	14-Mar-20																		
Award Districtwide Solar	52	15-Mar-20	05-May-20																		
Design Districtwide Solar	119	06-May-20	01-Sep-20																		
DSA Districtwide Solar	65	02-Sep-20	05-Nov-20																		
NTP PCC Construction Solar	0	06-Nov-20																			
PCC Construction Solar	120	06-Nov-20	05-Mar-21																		
NTP LAC Construction Solar	0	25-Jan-21																			
LAC Construction Solar	120	25-Jan-21	24-May-21																		
Expected Substantial Completion PCC Solar	0		05-Mar-21																		
Expected Substantial Completion LAC Solar	0		24-May-21																		
SCE Charge Ready																					
Design SCE Charge Ready	115	01-Apr-19 A	25-Jul-19																		

- PRE
- Bid /Award
- CONST
- Actual
- DESIGN
- DSA
- FF&E
- Milestone
- Milestone

