

LBCC Bond Program Master Schedule

Status as of June 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Long Beach Community College Bond Program Schedule - June 1, 2019																						
Liberal Arts Campus																						
Building J - Auditorium																						
Design Building J	176	01-Oct-15 A	24-Mar-16 A																			
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A																			
DSA Building J	398	03-Sep-16 A	06-Oct-17 A																			
Construction Building J (Spring 2018 - Fall 2019)	649	12-Jan-18 A	22-Oct-19																			
FF&E / Move Management from Building J from Public Theater & Building FF	301	24-Aug-19	19-Jun-20																			
Expected Substantial Completion Building J	0		22-Oct-19																			
Ready to Hold Classes Building J (Fall 2020)	0		19-Jun-20																			
Low Davis Sidewalk Replacement Project																						
Bid / Award Low Davis Sidewalk Replacement	89	11-Apr-19 A	08-Jul-19																			
NTP Low Davis Sidewalk Replacement	0	09-Jul-19																				
Construction Low Davis Sidewalk Replacement	40	09-Jul-19	17-Aug-19																			
Expected Substantial Completion	0		17-Aug-19																			
Kinesiology Labs & Aquatics Center																						
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A																			
Design Kinesiology Labs & Aquatic Center	615	01-Jun-17 A	06-Feb-19 A																			
DSA Kinesiology Labs & Aquatic Center	172	29-Jan-19 A	19-Jul-19																			
Bid / Award Kinesiology Labs & Aquatic Center	108	20-Jul-19	04-Nov-19																			
Construction Kinesiology Labs & Aquatic Center	530	05-Nov-19	17-Apr-21																			
NTP Kinesiology Labs & Aquatic Center	0	14-Nov-19																				
FF&E / Move Management Kinesiology Labs & Aquatic Center	194	18-Jan-21	30-Jul-21																			
Expected Substantial Completion Kinesiology Labs & Aquatic Center	0		17-Apr-21																			
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)	0		30-Jul-21																			
Building X - Central Plant Expansion																						
Design	413	23-Jan-18 A	12-Mar-19 A																			
DSA LAC Central Plant	66	13-Apr-19 A	17-Jun-19																			
Bid / Award	77	18-Jun-19	02-Sep-19																			
Construction LAC Central Plant	130	10-Sep-19	17-Jan-20																			
Expected Substantial Completion	0		17-Jan-20																			
LAC Site Barrier Removal																						
Design Campus Improvements	281	06-Oct-17 A	13-Jul-18 A																			
DSA Review LAC Site Barrier Removal	182	30-Nov-19	29-May-20																			
Bid / Award LAC Site Barrier Removal	90	30-May-20	27-Aug-20																			
Construction LAC Site Barrier Removal	518	03-Sep-20	02-Feb-22																			
Expected Substantial Completion	0		02-Feb-22																			
LAC Building Barrier Removal																						
Design Campus Improvements	281	06-Oct-17 A	13-Jul-18 A																			
DSA Review LAC Building Barrier Removal	182	28-Dec-19	26-Jun-20																			
Bid / Award LAC Building Barrier Removal	90	27-Jun-20	24-Sep-20																			
Construction LAC Building Barrier Removal	518	10-Oct-20	11-Mar-22																			
Expected Substantial Completion	0		11-Mar-22																			
Building B Renovation (Building M Swing Space)																						
Bid / Award Building B Swing Space for Building M	86	13-Apr-19 A	07-Jul-19																			
NTP Construction	0	08-Jul-19																				

Legend:

- Construction Building J (Spring 2018 - Fall 2019)
- FF&E / Move Management from Building J from Public Theater & Building FF
- ◆ Expected Substantial Completion Building J
- ◆ Ready to Hold Classes Building J (Fall 2020)

- Bid / Award Low Davis Sidewalk Replacement
- ◆ NTP Low Davis Sidewalk Replacement
- Construction Low Davis Sidewalk Replacement
- ◆ Expected Substantial Completion

- DSA Kinesiology Labs & Aquatic Center
- Bid / Award Kinesiology Labs & Aquatic Center
- Construction Kinesiology Labs & Aquatic Center
- ◆ NTP Kinesiology Labs & Aquatic Center
- FF&E / Move Management Kinesiology Labs & Aquatic Center
- ◆ Expected Substantial Completion Kinesiology Labs & Aquatic Center
- ◆ Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)

- DSA LAC Central Plant
- Bid / Award
- Construction LAC Central Plant
- ◆ Expected Substantial Completion

- DSA Review LAC Site Barrier Removal
- Bid / Award LAC Site Barrier Removal
- Construction LAC Site Barrier Removal
- ◆ Expected Substantial Completion

- DSA Review LAC Building Barrier Removal
- Bid / Award LAC Building Barrier Removal
- Construction LAC Building Barrier Removal
- ◆ Expected Substantial Completion

- Bid / Award Building B Swing Space for Building M
- ◆ NTP Construction


Legend:

- PRE
- Bid / Award
- CONST
- Actual
- DESIGN
- DSA
- FF&E
- Milestone

LBCC Bond Program Master Schedule

Status as of June 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Design Building O2	280	11-Oct-23	16-Jul-24																		
DSA Review Building O2	280	17-Jul-24	22-Apr-25																		
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25																		
Bid / Award Building O2	90	23-Apr-25	21-Jul-25																		
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25																		
Move Into Swing Space Building B for Building O2	20	22-Jun-25	11-Jul-25																		
NTP Construction Building O2	0	27-Jul-25																			
Construction Building O2	520	27-Jul-25	28-Dec-26																		
FF&E / Move Management from Building B to Building O2	209	09-Dec-26	05-Jul-27																		
Expected Substantial Completion Building O2	0		28-Dec-26																		
Building G - Music																					
Pre-Design Building G	216	04-Aug-25*	07-Mar-26																		
Design Building G	273	08-Mar-26	05-Dec-26																		
DSA Review Building G	280	06-Dec-26	11-Sep-27																		
Design Swing Space for Building G	67	01-Jun-27	06-Aug-27																		
Bid / Award Swing Space for Building G	89	07-Aug-27	03-Nov-27																		
Bid / Award Building G	90	12-Sep-27	10-Dec-27																		
Construction Swing Space Building for G	40	04-Nov-27	13-Dec-27																		
Expected Substantial Completion Swing Space Building for G	0		13-Dec-27																		
Move Into Swing Space Building B for Building G	15	14-Dec-27	28-Dec-27																		
Construction Building G	750	29-Dec-27	16-Jan-30																		
Expected Substantial Completion Building G	0		16-Jan-30																		
FF&E / Move Management Building G from Building B	162	17-Jan-30	27-Jun-30																		
Ready to Hold Classes Building G	0		27-Jun-30																		
Building H - Theater Arts																					
Pre-Design Building H	217	04-Aug-25*	08-Mar-26																		
Design Building H	273	09-Mar-26	06-Dec-26																		
DSA Review Building H	280	07-Dec-26	12-Sep-27																		
Bid / Award Building H	92	13-Sep-27	13-Dec-27																		
Move Into Public Theater from Building H	20	14-Dec-27	02-Jan-28																		
Construction Building H	750	29-Dec-27	16-Jan-30																		
Expected Substantial Completion	0		16-Jan-30																		
FF&E / Move Management Building H from Building Public Theater	146	17-Jan-30	11-Jun-30																		
Ready to Hold Classes Building H	0		11-Jun-30																		
Building K - Art																					
Pre-Design Building K	210	06-Aug-28*	03-Mar-29																		
Design Building K	224	04-Mar-29	13-Oct-29																		
DSA Review Building K	280	14-Oct-29	20-Jul-30																		
Bid / Award Building K	90	21-Jul-30	18-Oct-30																		
Move Into Swing Space Building B for Building K	10	19-Dec-30	28-Dec-30																		
NTP Construction Building K	0	29-Dec-30																			
Construction Building K	390	29-Dec-30	22-Jan-32																		
FF&E / Move Management Building K from Building B	251	25-Oct-31	01-Jul-32																		
Expected Substantial Completion Building K	0		22-Jan-32																		
Ready to Hold Classes Building K	0		01-Jul-32																		
Building R - Primary Gymnasium																					
Pre-Design Building R	145	08-Jul-29*	29-Nov-29																		

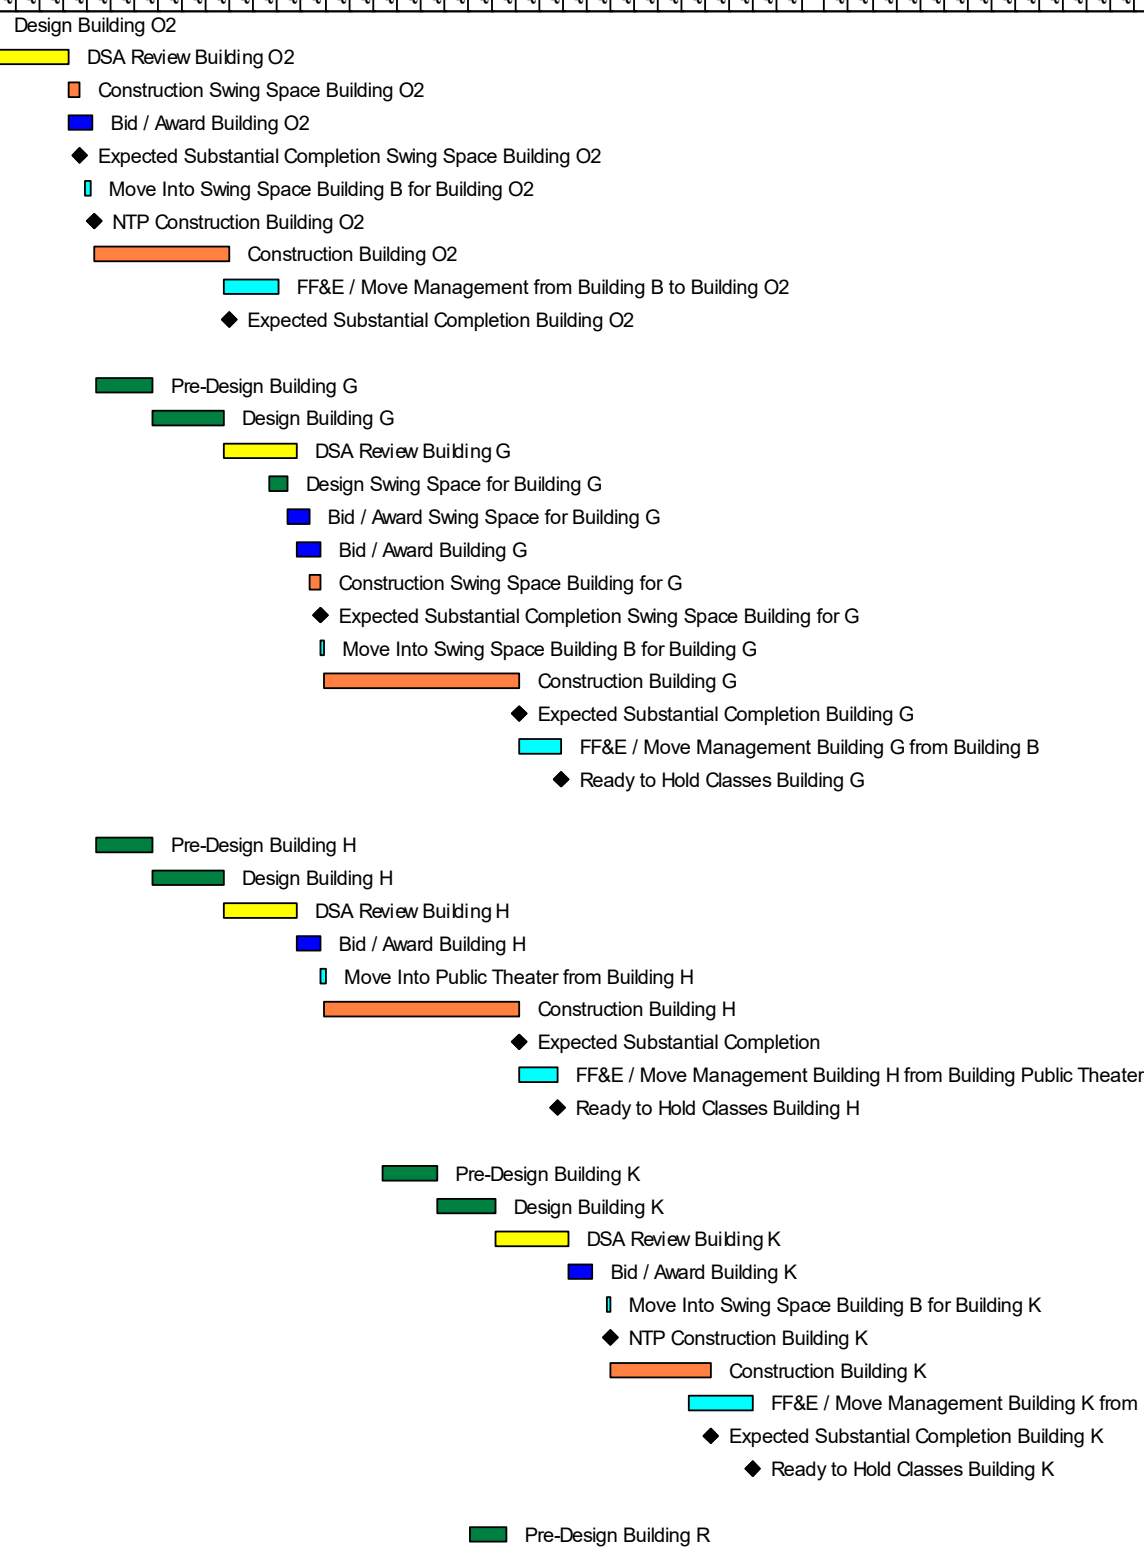


■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of June 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Design Building R	363	30-Nov-29	27-Nov-30																			
DSA Review Building R	280	28-Nov-30	03-Sep-31																			
Bid / Award Building R	90	04-Sep-31	02-Dec-31																			
NTP Construction Building R	0	08-Dec-31																				
Construction Building R	730	08-Dec-31	06-Dec-33																			
FF&E / Move Management Building R	180	10-Jul-33	05-Jan-34																			
Expected Substantial Completion Building R	0		06-Dec-33																			
Ready to Hold Classes Building R	0		05-Jan-34																			
Building Q - Secondary Gymnasium																						
Pre-Design Building	320	16-Jun-31*	30-Apr-32																			
Design Building	246	01-May-32	01-Jan-33																			
DSA Review Building	280	02-Jan-33	08-Oct-33																			
Bid / Award Building	90	09-Oct-33	06-Jan-34																			
NTP Construction Building	0	12-Jan-34																				
Construction Building	640	12-Jan-34	13-Oct-35																			
FF&E / Move Management Building Q	195	16-Jun-35	27-Dec-35																			
Expected Substantial Completion Building	0		13-Oct-35																			
Ready to Hold Classes Building	0		27-Dec-35																			
Building B - Tech Studies																						
Pre-Design Building	200	18-Aug-32*	05-Mar-33																			
Design Building	276	06-Mar-33	06-Dec-33																			
DSA Review Building	280	07-Dec-33	12-Sep-34																			
Bid / Award Building	90	13-Sep-34	11-Dec-34																			
NTP Construction Building	0	12-Dec-34																				
Construction Building	730	28-Dec-34	26-Dec-36																			
Expected Substantial Completion Building	0		26-Dec-36																			
Building F - Demo Family/Consumer Education/New Courtyard																						
Design Building F	245	03-Mar-35*	02-Nov-35																			
DSA Review Building F	160	03-Nov-35	10-Apr-36																			
Bid / Award Building F	55	11-Apr-36	04-Jun-36																			
Move Into Building B from Building F	180	27-Dec-36	24-Jun-37																			
Demo & Courtyard Building F	365	25-Jun-37	24-Jun-38																			
Building O1 - IITS/ Warehouse																						
Pre-Design Building	183	02-May-35*	31-Oct-35																			
Design Building	244	01-Nov-35	01-Jul-36																			
DSA Review Building	280	02-Jul-36	07-Apr-37																			
Bid / Award Building	90	08-Apr-37	06-Jul-37																			
NTP Construction Building	0	12-Jul-37																				
Construction Building O1	420	12-Jul-37	04-Sep-38																			
FF&E / Move Management Building O1 from Building O2	213	08-May-38	06-Dec-38																			
Expected Substantial Completion Building O1	0		04-Sep-38																			
Building S - Stadium																						
Pre-Design Building	200	01-May-35*	16-Nov-35																			
Design Building	365	22-Nov-35	20-Nov-36																			
DSA Review Building S	280	21-Nov-36	27-Aug-37																			
Bid / Award Building S	90	28-Aug-37	25-Nov-37																			
Construction Swing Space Building for S	90	28-Aug-37	25-Nov-37																			

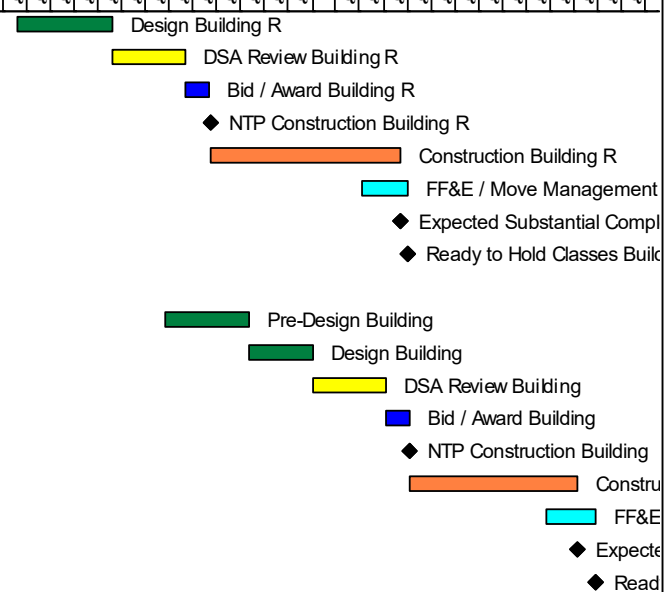

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of June 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Expected Substantial Completion Swing Space Building for S	0		25-Nov-37																				
Move Into Swing Space Building TBD from Building S	15	06-Dec-37	20-Dec-37																				
NTP Construction Building S	0	21-Dec-37																					
Construction Building S	700	21-Dec-37	20-Nov-39																				
FF&E / Move Management Building from Building TBD to Building S	250	24-Jul-39	29-Mar-40																				
Expected Substantial Completion Building S	0		20-Nov-39																				
Punchlist Building S	30	21-Nov-39	20-Dec-39																				
Ready to Hold Classes Building S	0		29-Mar-40																				
Building CDC - Child Development Center																							
Pre-Design Building	49	01-Jun-37*	19-Jul-37																				
Design Building	154	20-Jul-37	20-Dec-37																				
DSA Review Building	280	21-Dec-37	26-Sep-38																				
Bid / Award Building	90	27-Sep-38	25-Dec-38																				
NTP Construction Building	0	26-Dec-38																					
Construction Building	290	26-Dec-38	11-Oct-39																				
FF&E / Move Management	201	13-Jun-39	30-Dec-39																				
Expected Substantial Completion Building	0		11-Sep-39																				
Pacific Coast Campus																							
PCC Building Barrier Removal																							
Bid / Award Building Barrier Removal	117	20-Feb-18 A	17-Jun-18 A																				
Construction - Phase 0	69	24-Jul-18 A	01-Oct-18 A																				
Construction - Phase 1-A	143	10-Sep-18 A	31-Jan-19 A																				
Construction - Phase 1-B	227	10-Sep-18 A	25-Apr-19 A																				
Construction - Phase 2	126	18-Jan-19 A	24-May-19 A																				
Construction - Phase 3	60	06-Jun-19	04-Aug-19																				
Construction - Phase 4	35	05-Aug-19	08-Sep-19																				
Expected Substantial Completion AI Phases	0		08-Sep-19																				
Building P2 - PCC Parking Structure																							
Design Parking Structure	224	16-Jul-18 A	25-Feb-19 A																				
DSA Review Parking Structure	217	16-Jan-19 A	20-Aug-19																				
NTP Construction Parking Structure	0	20-Aug-19																					
Construction Parking Structure	400	20-Aug-19	22-Sep-20																				
Expected Substantial Completion Parking Structure	0		22-Sep-20																				
Closeout Parking Structure	30	23-Sep-20	22-Oct-20																				
Building MM - Construction Trades Ph 1																							
DSA Review Building MM Ph 1	243	07-Jan-19 A	07-Sep-19																				
Bid / Award Building MM Ph 1	185	07-Sep-19	09-Mar-20																				
Construction Building MM Ph 1	420	10-Mar-20	03-May-21																				
FF&E / Move Management Building MM for Building MM Ph 1	192	03-Feb-21	13-Aug-21																				
Expected Substantial Completion Building MM Ph 1	0		03-May-21																				
Ready to Hold Classes Building MM Ph 1 (Fall 2021)	0		13-Aug-21																				
EEM-2A - Energy and Portable Water Reductions - PCC (TBD)																							
Design EEM-2A	180	01-Apr-20*	27-Sep-20																				
DSA EEM-2A	260	28-Sep-20	14-Jun-21																				
Bid / Award EEM-2A	90	15-Jun-21	12-Sep-21																				
Construction EEM-2A	365	13-Sep-21	12-Sep-22																				


- Construction - Phase 3
- Construction - Phase 4
- ◆ Expected Substantial Completion AI Phases
- DSA Review Parking Structure
- ◆ NTP Construction Parking Structure
- Construction Parking Structure
- ◆ Expected Substantial Completion Parking Structure
- Closeout Parking Structure
- DSA Review Building MM Ph 1
- Bid / Award Building MM Ph 1
- Construction Building MM Ph 1
- FF&E / Move Management Building MM for Building MM Ph 1
- ◆ Expected Substantial Completion Building MM Ph 1
- ◆ Ready to Hold Classes Building MM Ph 1 (Fall 2021)
- Design EEM-2A
- DSA EEM-2A
- Bid / Award EEM-2A
- Construction EEM-2A

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of June 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Building MM - Construction Trades Ph 2																							
Design Building MM Ph 2	454	01-Oct-20	28-Dec-21																				
DSA Review Building MM Ph 2	280	29-Dec-21	04-Oct-22																				
Bid / Award Building Building MM Ph 2	90	05-Oct-22	02-Jan-23																				
Construction Building MM Ph 2	390	03-Jan-23	27-Jan-24																				
FF&E / Move Management Building MM from Building MM Ph 2	238	29-Nov-23	23-Jul-24																				
Expected Substantial Completion Building MM Ph 2	0		27-Jan-24																				
Ready to Hold Classes Building MM Ph 2 (Fall 2024)	0		23-Jul-24																				
Building OO - Humanities																							
Design Building Humanities	608	01-Oct-20*	31-May-22																				
DSA Review Building Humanities	280	01-Jun-22	07-Mar-23																				
Bid / Award Building Humanities	90	08-Mar-23	05-Jun-23																				
NTP Construction Building Humanities	0		10-Jun-23																				
Construction Building Humanities	770	11-Jun-23	19-Jul-25																				
FF&E / Move Management Building Humanities from Building Humanities	270	11-Apr-25	05-Jan-26																				
Expected Substantial Completion Building Humanities	0		19-Jul-25																				
Ready to Hold Classes Building Humanities (Spring 2026)	0		05-Jan-26																				
Building FF - Demo Fine Arts & Senior Center/Turnabout																							
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23																				
DSA Review Building FF	280	09-Mar-23	13-Dec-23																				
Bid / Award Building FF Demo & Turnabout	86	14-Dec-23	08-Mar-24																				
Construction Building FF Demo	155	09-Mar-24	10-Aug-24																				
PCC Walkways & Wayfinding																							
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41																				
District Wide																							
Joint Use Facility w/ LBUSD & CSULB #12																							
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21																				
Energy/Water Conservation Projects																							
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41																				
Districtwide Solar Projects																							
Pre-Design, Criteria Documents, RFP	360	21-Mar-19 A	14-Mar-20																				
Award Districtwide Solar	40	15-Mar-20	23-Apr-20																				
Design Districtwide Solar	112	24-Apr-20	13-Aug-20																				
DSA Review Districtwide Solar	120	14-Aug-20	11-Dec-20																				
NTP PCC Construction Solar	0	12-Dec-20																					
PCC Construction Solar	120	12-Dec-20	10-Apr-21																				
NTP LAC Construction Solar	0	10-Feb-21																					
LAC Construction Solar	120	10-Feb-21	09-Jun-21																				
Expected Substantial Completion PCC Solar	0		10-Apr-21																				
Expected Substantial Completion LAC Solar	0		09-Jun-21																				
SCE Charge Ready																							
Design SCE Charge Ready	100	01-Apr-19 A	09-Jul-19																				
PCC Construction Infrastructure SCE Charge Ready	60	01-May-19 A	29-Jun-19																				
PCC Construction Install ChargePoint SCE Charge Ready	60	30-Jun-19	28-Aug-19																				
Easement SCE Charge Ready	56	09-Jul-19	03-Sep-19																				
DSA SCE Charge Ready	72	09-Jul-19	19-Sep-19																				

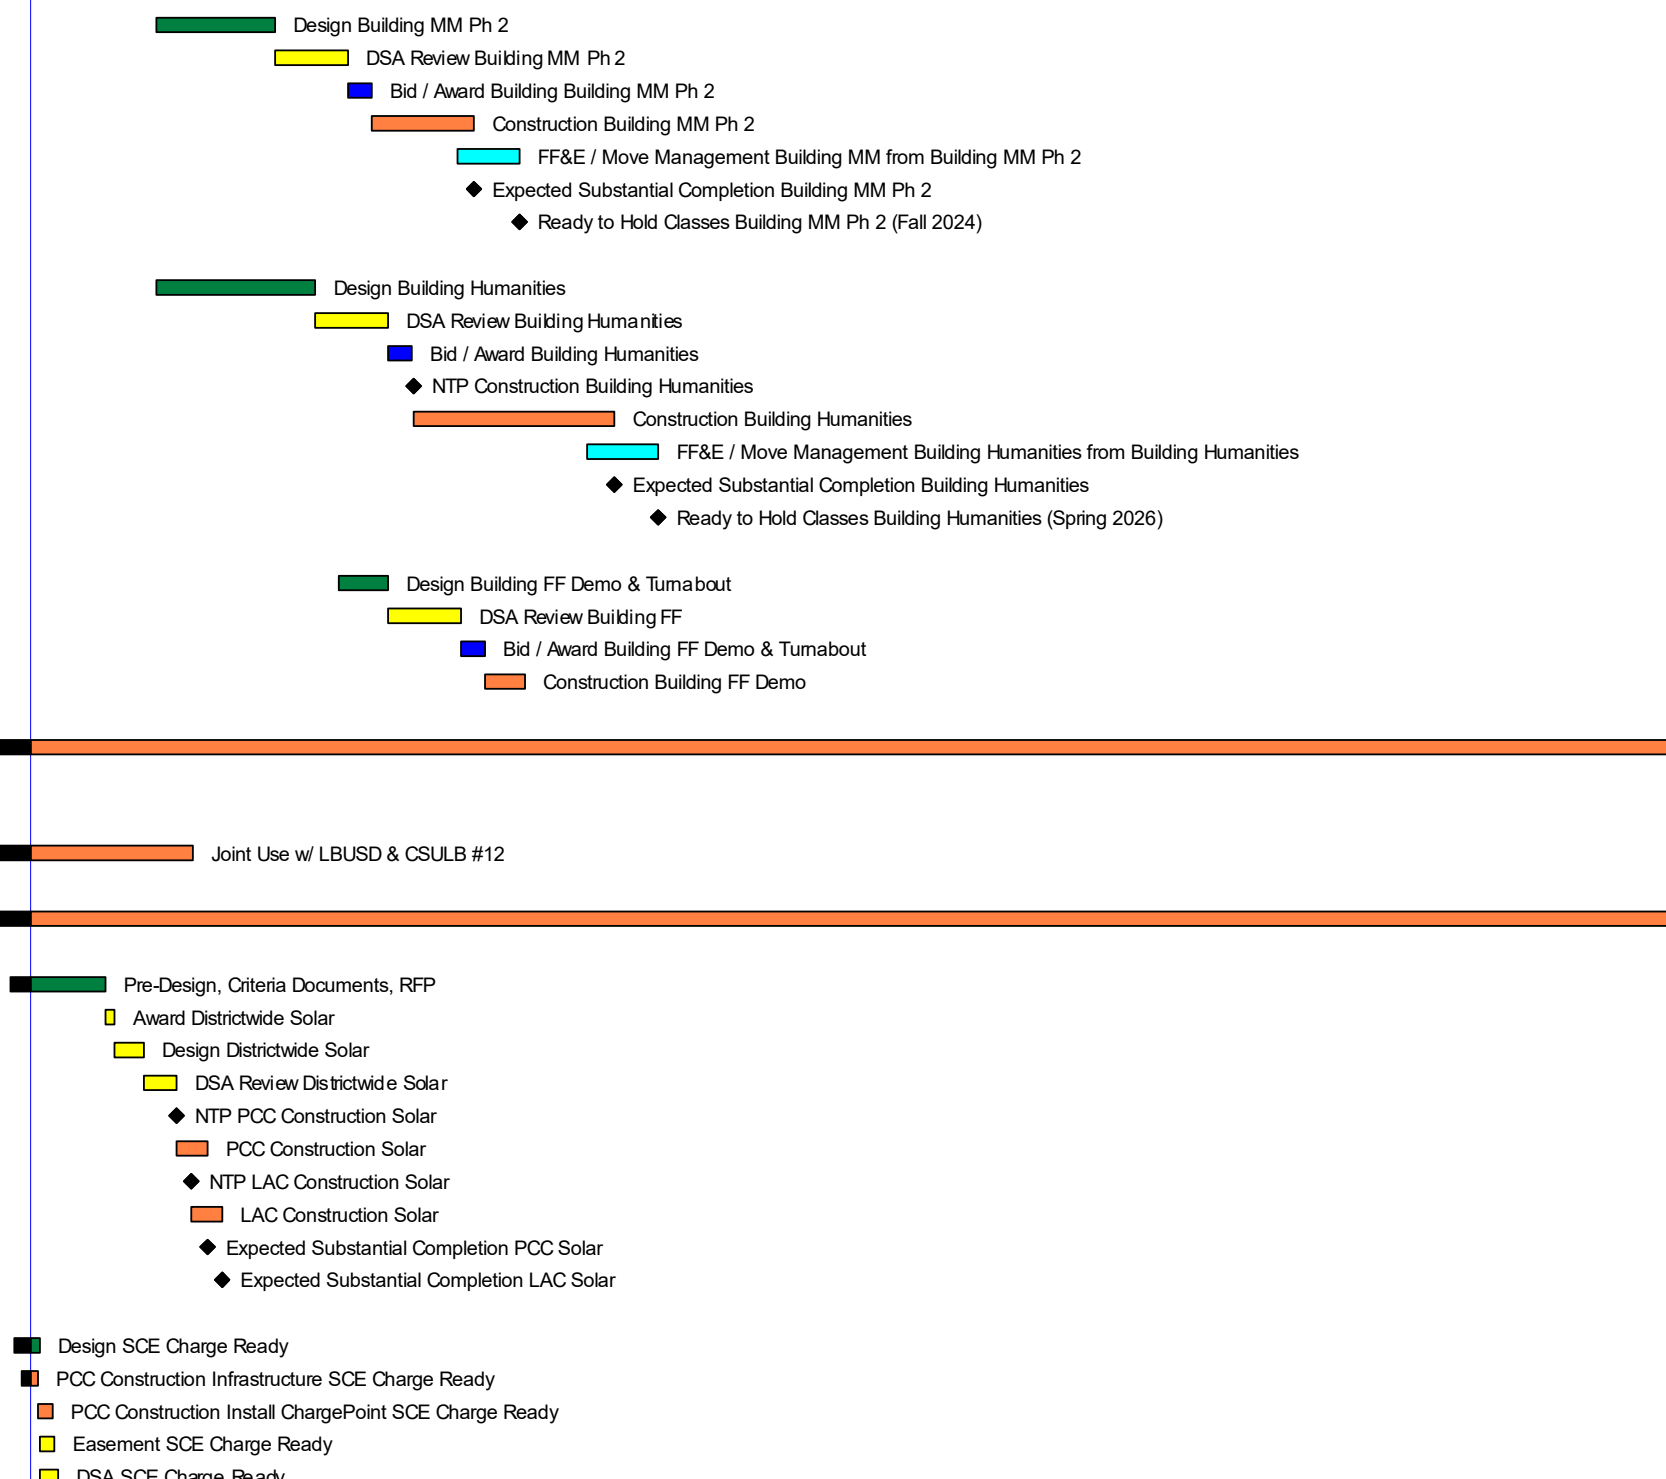

■ PRE ■ Bid/Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone

LBCC Bond Program Master Schedule

Status as of June 1, 2019

Activity Name	At Completion Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
LAC Construction SCE Infrastructure SCE Charge Ready	60	19-Sep-19	18-Nov-19	<div style="display: flex; justify-content: space-between;"> ■ LAC Construction SCE Infrastructure SCE Charge Ready </div>																		
LAC Construction Install ChargePoint SCE Charge Ready	60	18-Nov-19	17-Jan-20	<div style="display: flex; justify-content: space-between;"> ■ LAC Construction Install ChargePoint SCE Charge Ready </div>																		
Technology Refresh/Replacement																						
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41																			
Enterprise Wide Computer System																						
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41																			
Landscaping																						
Landscaping	8923	01-Feb-17 A	07-Jul-41																			
Infrastructure Projectss																						
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41																			
Minor Campus Improvements																						
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41																			
Surface Parking Improvements																						
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41																			

■ PRE ■ Bid /Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone
